

H296-C1

Laurence G. Hanscom Field

**REHABILITATE TAXIWAY E FROM TAXIWAY M TO RUNWAY 5-23
AND CONSTRUCT TAXIWAY E5
Pre-Bid Conference**

BEDFORD, MA



H296-CI Rehabilitate Taxiway E From Taxiway M to Runway 5-23 and Construct Taxiway E5 Project

Agenda

Expected Outcome: *An understanding of the H296-CI project description and contract requirements*

- Contract Overview
- Project Requirements
- Scope of Work
- Submission Schedule



Attendees: Please enter your name and contact information in the Zoom chat

H296-CI Rehabilitate Taxiway E From Taxiway M to Runway 5-23 and Construct Taxiway E5 Project

Contract Overview & Project Requirements

- 5% Bid Deposit
- Bidders must submit a Buy American Certificate with all bids or offers on Federal (Airport Improvement Program) funded projects; this project will be FAA funded.
- This Contract has a DBE goal of 15.7%
- The estimated contract cost \$ 5,137,354.00
- Airport Security (SIDA) Badge
- Anticipated NTP for mobilization is on or about July 1, 2025
- Anticipated NTP for Construction is August 4th, 2025
- The total duration of the construction project is 71 calendar days, with Milestone 1 set at 30 calendar days and Milestone 2 at 41 calendar days

H296-CI Rehabilitate Taxiway E From Taxiway M to Runway 5-23 and Construct Taxiway E5 Project

Scope of Work

- Pavement Milling
- Earthwork (Excavation and Embankment)
- Hot Mix Asphalt Paving
- Crack Repairs
- Adjustment of Airfield Light Fixtures
- Light Fixture Installation
- Pavement Sealing
- Pavement Markings
- Airfield Guidance Sign Modifications
- Topsoiling and Seeding

H296-CI Rehabilitate Taxiway E From Taxiway M to Runway 5-23 and Construct Taxiway E5 Project

Contract Overview & Project Requirements

PROJECT MILESTONES

A. MILESTONE 1: 30 CALENDAR DAYS

PHASE 1 MUST BE COMPLETED WITHIN 20 CALENDAR DAYS OF THE CONSTRUCTION NOTICE TO PROCEED.

PHASE 2 MUST BE COMPLETED WITHIN 10 CALENDAR DAYS OF THE CONSTRUCTION TO PROCEED.

B. MILESTONE 2: 41 CALENDAR DAYS (SPRING 2026)


PHASE 3 (INCLUSIVE OF ALL LIGHT ADJUSTMENTS) MUST BE COMPLETED WITHIN 36 NIGHT AND 2 WEEKEND RUNWAY CLOSURE, WHICH BEGINS ON THE DAY OF CONSTRUCTION NOTICE TO PROCEED. THE NIGHT RUNWAY CLOSURE IS DEFINED AS THE CLOSURE OF RUNWAY 11-29 THAT PROHIBITS ALL LANDING AND TAKEOFF OPERATIONS ON THE RUNWAY BETWEEN THE HOURS OF 10:00 PM TO 6:00 AM MONDAY TO FRIDAY. WEEKEND RUNWAY CLOSURES ARE FROM FRIDAY 10:00 PM TO SUNDAY 2:00 PM WHERE LANDING AND TAKEOFF OPERATIONS ON THE RUNWAY 11-29 ARE PROHIBITED.

AFTER 30 DAYS CURING, FINISH FINAL PAVEMENT MARKING FOR TAXIWAY E5. RUNWAY CLOSURE TO FINISH THIS WORK WILL NEED TO BE COORDINATED WITH AIRPORT OPERATIONS.

- **Liquidated Damages** will be assessed at **\$5,000 per calendar day** if schedule not achieved
- Safety Plan Compliance Document (SPCD)
- Anticipate weekly on-site construction meetings


H296-CI Rehabilitate Taxiway E From Taxiway M to Runway 5-23 and Construct Taxiway E5 Project

Project Phases & Contractor Staging Area

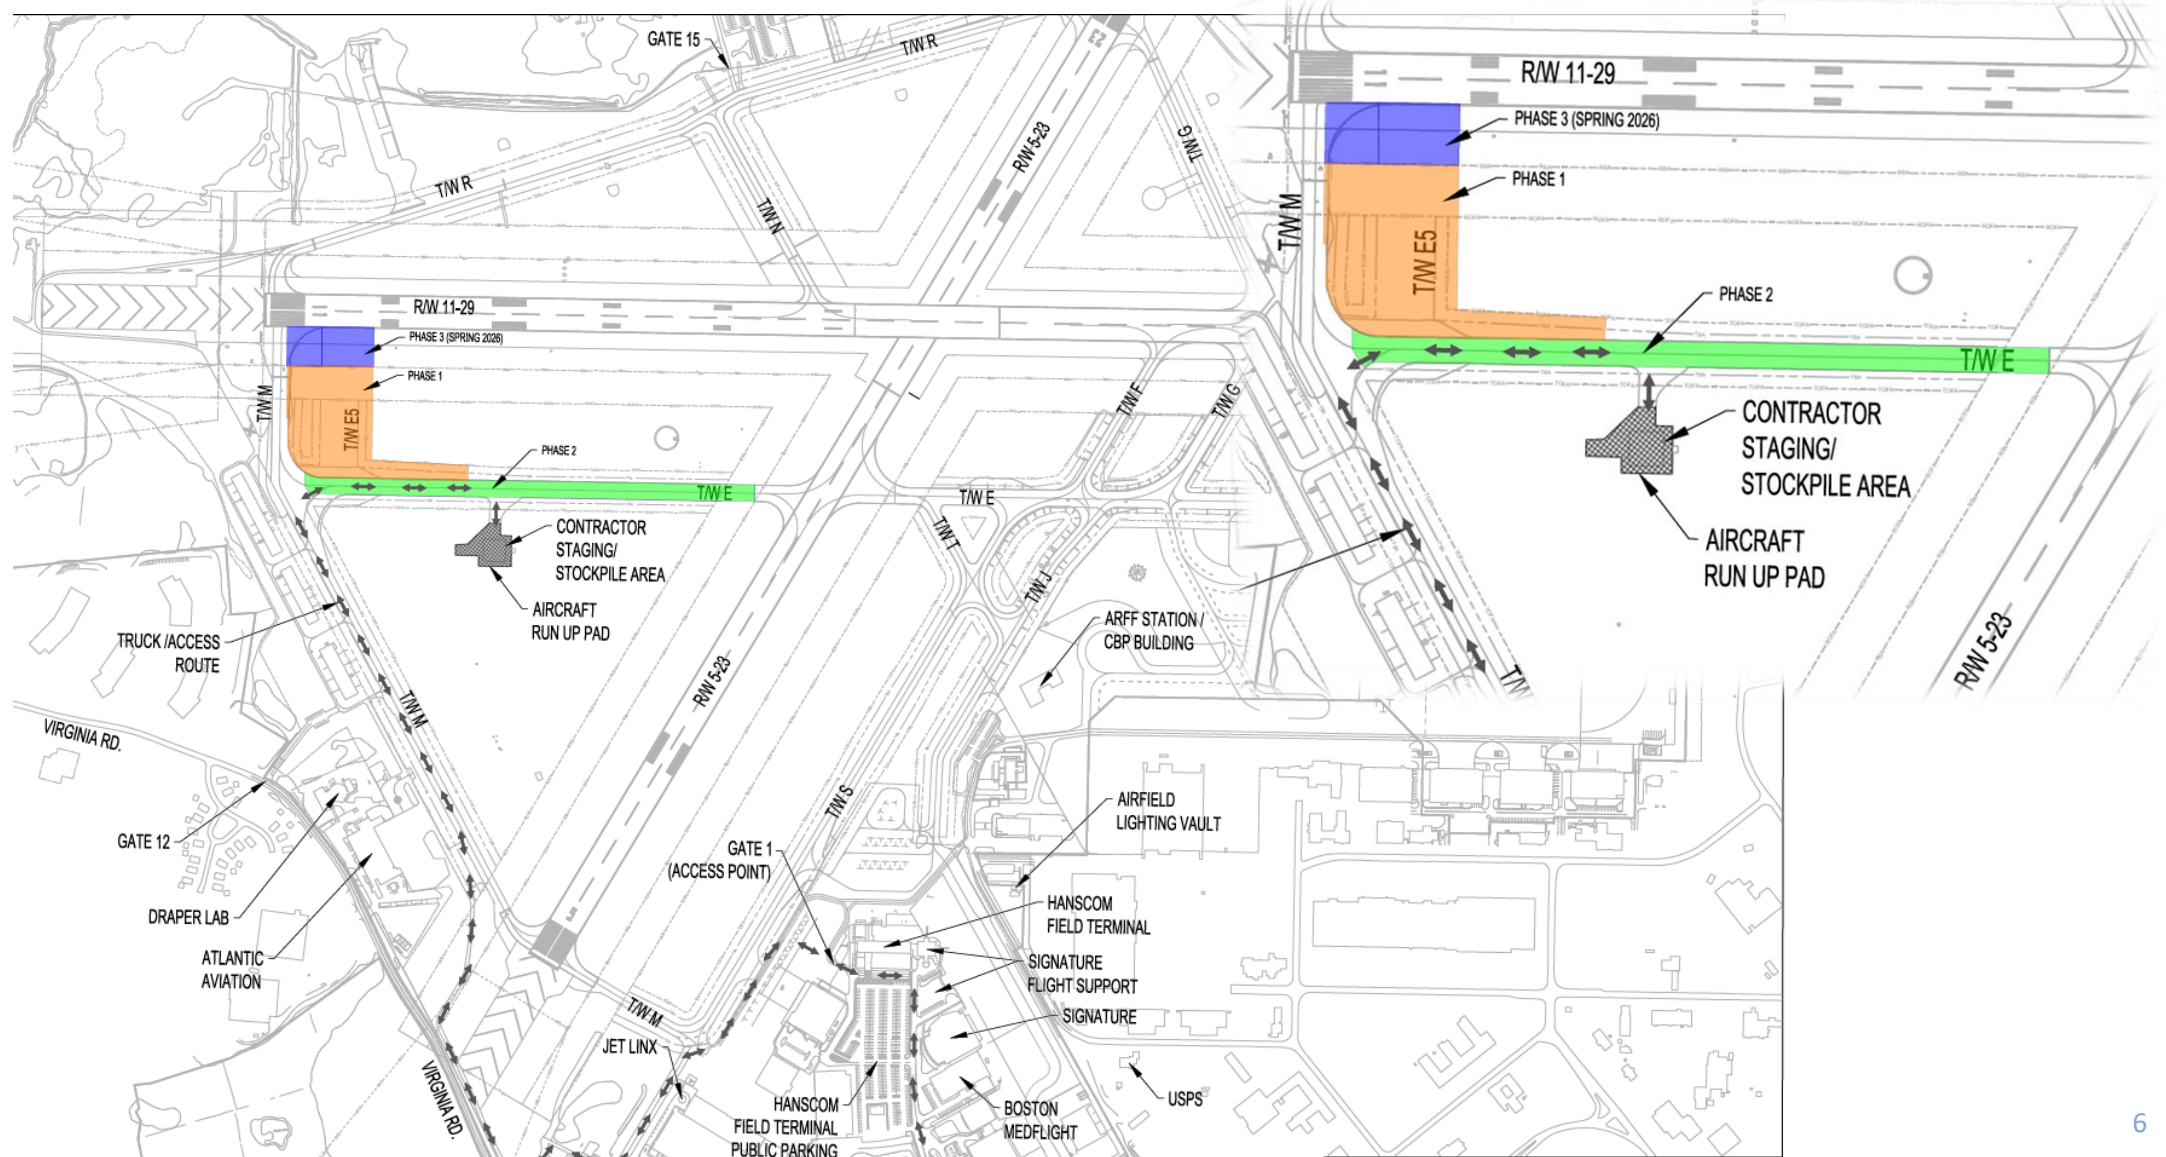

H296-CI Rehabilitate Taxiway E From Taxiway M to Runway 5-23 and Construct Taxiway E5 Project

Proposed Contractor's Haul Route

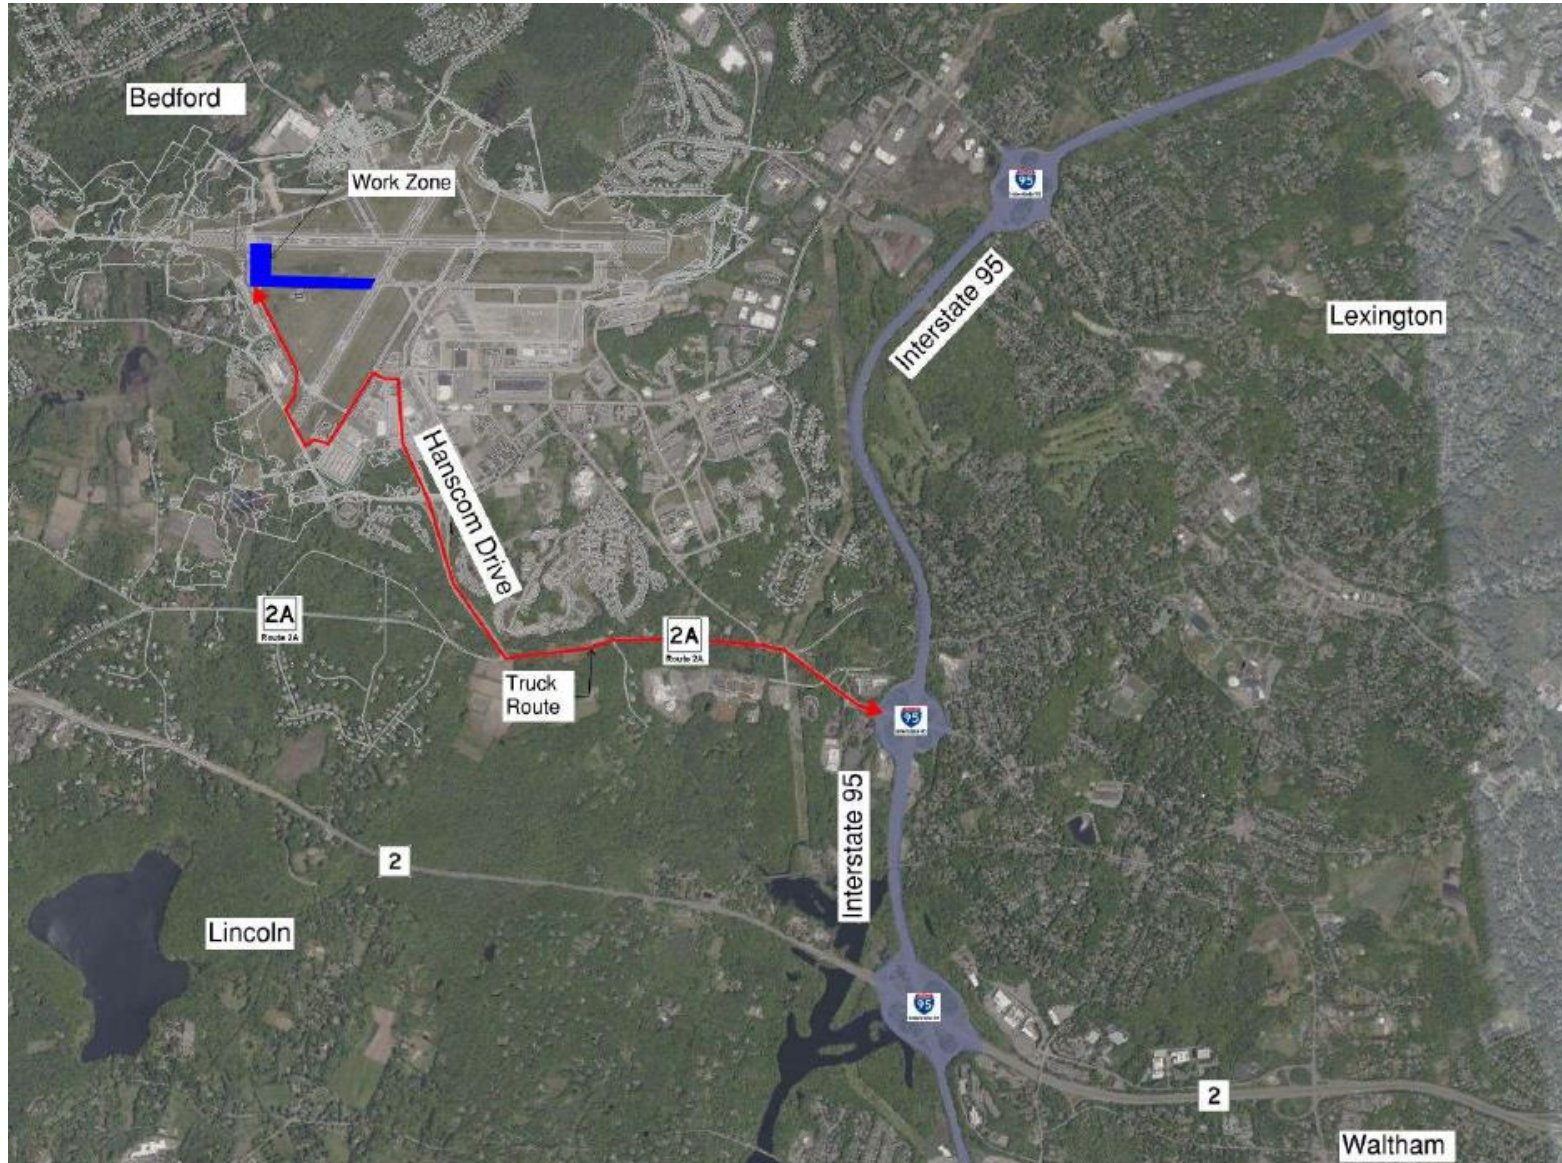

H296-CI Rehabilitate Taxiway E From Taxiway M to Runway 5-23 and Construct Taxiway E5 Project

Submission Schedule

❖ **April 8, 5:00 pm**

❖ **April 11 (estimated)**

❖ **April 16, 11:00 am**

Written GC questions submitted to:

CPBidQuestions@massport.com

Massport published responses

General bids due (electronic)



THANK YOU
